



# Port Owen Marina Authority (NPC)

Reg # 1999/010199/08

PostNet Suite 2 Private Bag X1 Vredenburg 7380 · Tel 022 783 0943 · Fax 0865462112

· E-mail: poma@poma.co.za

## Weekly dredge monitoring report

Dredge area 3B: Eastern Loop Channel was dredged between 12 and 16 January 2026 (hereafter referred to as “Week 2”). The stipulated conditions allowing for dredging and discharge from the settling dam include an outgoing current equal to or greater than  $0.43 \text{ m.s}^{-1}$  (equivalent to site specific  $200 \text{ m}^3.\text{s}^{-1}$ ), only between sunrise and sunset, and only on weekdays (excluding public holidays). Operational conditions for release require that dredging only occur when these parameters allowed for at least 1 hour of dredging to the river. As a result of these parameters, only 2 dredge sessions could occur for Week 2 of January 2026, as per dredge schedule. Up to five additional dredge sessions were possible under correct river velocity, of which 4 occurred. No dredging to and no discharge from the settling dam occurred (Table 1). For Week 2 of January 2026 a volume of  $1224 \text{ m}^3$  was dredged from area 3B and no blockages of the suction head occurred (Table 1).


**Table 1. Operational dredging variables.**

Dredging of Dredge area 3B	Total
Allowable dredge sessions	6
Dredge sessions to river	6
Dredge sessions to settling dam	0
Release from settling dam	0
Dredge volume ( $\text{m}^3$ )	1224
Stop incidents (due to blockage)	0

A total engine run time of 11 hours, and 47 minutes was achieved for Week 2 of January 2026 with a mean run time of 1 hour and 57 minutes per dredge session (Table 2). The mean dredge time achieved per session was 1 hour and 41 minutes, indicating zero minutes stoppage time due to blockages of the suction head (Table 2). The mean volume of dredge material discharged to the river was  $204 \text{ m}^3$  per session (Table 2).

**Table 2. Operational variables and means per dredge session.**

Operational variables	Total	Mean (per session)
Engine time (h:min)	11:47	1:57
Dredge time (h:min)	10:11	1:41
Stoppage time (h:min)	0	0
Volume direct to river ( $\text{m}^3$ )	1224	204
Volume to dam ( $\text{m}^3$ )	0	0
Volume from dam to river ( $\text{m}^3$ )	0	0

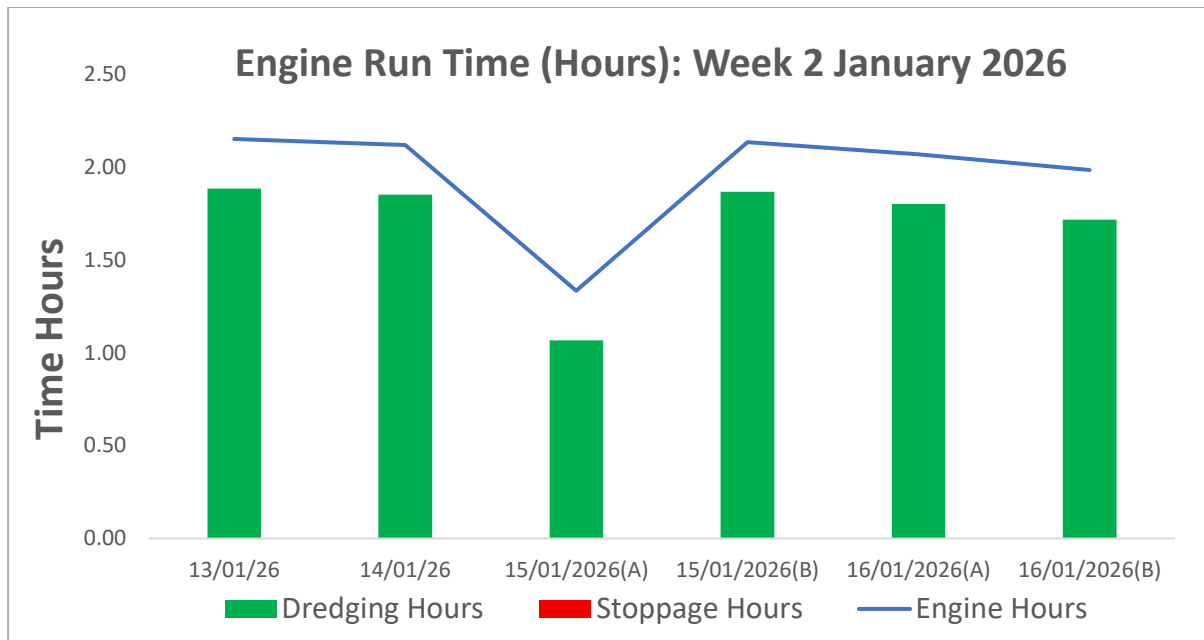

## River velocity

Mean river velocity recorded before, during, and after dredging remained within the allowable parameter (above 0.43 m.s<sup>-1</sup>) for Week 2 of January 2026 dredging (Table 3).

**Table 3. Mean river velocity before, during, and after dredging.**

River velocity	Mean (m.s <sup>-1</sup> )
Before dredging	0.45
During dredging	0.59
After dredging	0.58

