



Port Owen Marina Authority (NPC)

Reg # 1999/010199/08

PostNet Suite 2 Private Bag X1 Vredenburg 7380 · Tel 022 783 0943 · Fax 0865462112

· E-mail: poma@poma.co.za

Weekly dredge monitoring report

Dredge area 3B: Eastern Entrance was dredged between 18 and 22 May 2026 (hereafter referred to as “Week 2”). The stipulated conditions allowing for dredging and discharge from the settling dam include an outgoing current equal to or greater than $0.43 \text{ m}\cdot\text{s}^{-1}$ (equivalent to site specific $200 \text{ m}^3\cdot\text{s}^{-1}$), only between 6am and 8pm, and only on weekdays (excluding public holidays). Operational conditions for release require that dredging only occur when these parameters allowed for at least 1 hour of dredging. As a result of these parameters, 5 dredge sessions could occur for Week 2 of May 2026, of which 1 was cancelled due to a breakdown on the 18th May 2026. No dredging to and no discharge from the settling dam occurred (Table 1). For Week 2 of May 2026 a volume of 1420.7 m^3 was dredged from area 3B and blockages of the suction head occurred 2 times due to seaweed (Table 1).


Table 1. Operational dredging variables.

Dredging of Dredge area 3A	Total
Allowable dredge sessions	5
Dredge sessions to river	4
Dredge sessions to settling dam	0
Release from settling dam	0
Dredge volume (m^3)	1420.7
Stop incidents (due to blockage)	2

A total engine run time of 12 hours, and 19 minutes was achieved for Week 2 of May 2026 with a mean run time of 3 hours and 4 minutes per dredge session (Table 2). The mean dredge time achieved per session was 2 hours and 45 minutes, indicating 3 minutes of stoppage time due to blockages of the suction head (Table 2). The mean volume of dredge material discharged to the river was 355.2 m^3 per session (Table 2).

Table 2. Operational variables and means per dredge session.

Operational variables	Total	Mean (per session)
Engine time (h:min)	12:19	3:04
Dredge time (h:min)	11:03	2:45
Stoppage time (h:min)	0:12	0:03
Volume direct to river (m^3)	1420.7	355.2
Volume to dam (m^3)	0	0
Volume from dam to river (m^3)	0	0

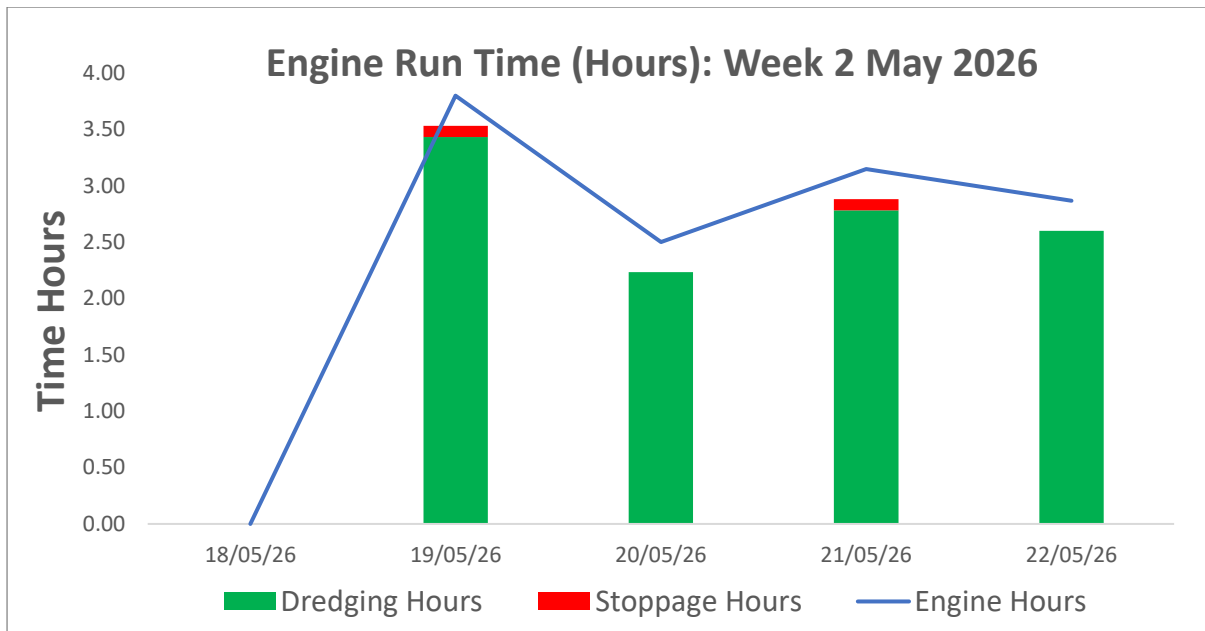

River velocity

Mean river velocity recorded before, during, and after dredging remained within the allowable parameter (above 0.43 m.s⁻¹) for Week 2 of May 2026 dredging (Table 3).

Table 3. Mean river velocity before, during, and after dredging.

River velocity	Mean (m.s ⁻¹)
Before dredging	0.79
During dredging	0.87
After dredging	0.84

